

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1		**Phase 1A: Project Proposal and Planning**	**10 days**	**Thu 9/3/26**	**Wed 9/16/26**		
10		**Phase 1B: Detailed Scheduling & WBS**	**7 days**	**Thu 9/10/26**	**Fri 9/18/26**		
19		**Phase 2: Requirements & Architecture**	**8 days**	**Wed 9/16/26**	**Fri 9/25/26**		**Conner Cowles,Jennifer Sanchez,Jonathar**
20		**2.1 System Architecture & Database Design**	**4 days**	**Wed 9/16/26**	**Mon 9/21/26**		**Jonathan Wesley,Conner Cowles,Jennifer**
21		2.1.1 Draw the system map and setup network diagrams	2 days	Wed 9/16/26	Thu 9/17/26		Jonathan Wesley
22		2.1.2 Identify system components and technology stack	2 days	Wed 9/16/26	Thu 9/17/26		Jonathan Wesley
23		2.1.3 Make the database layout and table relationships	15 days	Mon 9/21/26	Fri 10/9/26		Jonathan Wesley

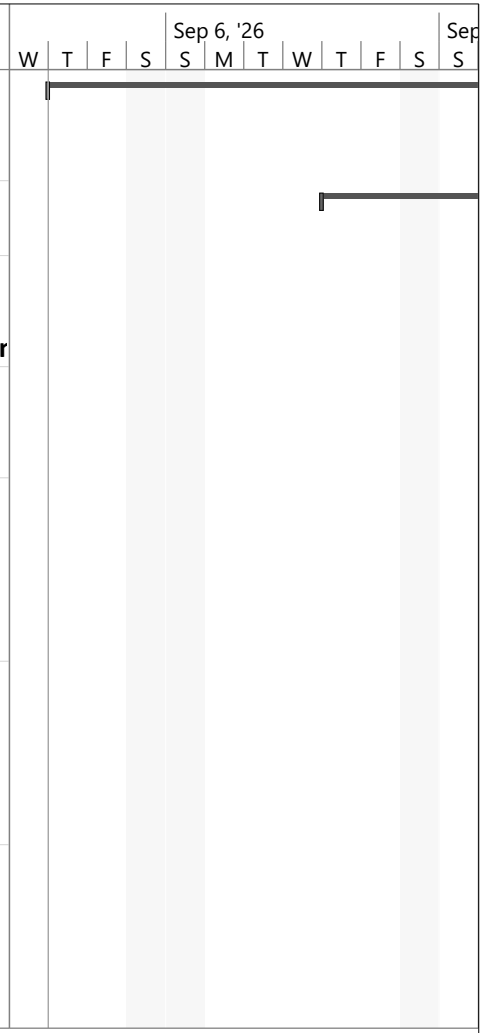


Project: IT Capstone Project- Iss
Date: Fri 10/30/26

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
24		2.1.4 Define user roles and permissions	2 days	Wed 9/16/26	Thu 9/17/26		Jennifer Sanchez,Jonathan Wesley
25		2.1.5 Define employee onboarding/offb	2 days	Wed 9/16/26	Thu 9/17/26		Conner Cowles,Jennifer Sanchez,Jonathan
26		**2.2 Software Requirements**	**5 days**	**Wed 9/16/26**	**Tue 9/22/26**	**20**	**Jennifer Sanchez,Paul**
27		2.2.1 Write down what the system needs to do and how it should perform	2 days	Wed 9/16/26	Thu 9/17/26	21	Jennifer Sanchez,Paul Intriago Troya
28		2.2.2 Define function and non-functional requirements	2 days	Thu 9/17/26	Fri 9/18/26	27	Jennifer Sanchez,Paul Intriago Troya
29		2.2.3 Sketch screen layouts and step by step user paths	3 days	Fri 9/18/26	Tue 9/22/26	27,28	Paul Intriago Troya,Conner Cowles
30		2.2.4 Define onboarding checklist requirements	2 days	Tue 9/22/26	Wed 9/23/26	29	Conner Cowles,Yadriel Quinones Sustache




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
31		2.2.6 Define offboarding checklist requirements	2 days	Tue 9/22/26	Wed 9/23/26		Jennifer Sanchez
32		2.2.7 Define equipment/inve requirements	1 day	Wed 9/23/26	Wed 9/23/26		Jennifer Sanchez
33		2.2.8 Define help-desk requirements	1 day	Wed 9/23/26	Wed 9/23/26		Conner Cowles,Jennifer Sanchez,Jonathan
34		**2.3 Development Planning**	**3 days**	**Thu 9/24/26**	**Mon 9/28/26**		**Conner Cowles,Jennifer**
35		2.3.1 Crete GitHub repository and	1 day	Thu 9/24/26	Thu 9/24/26		Jonathan Wesley
36		2.3.2 Create development branches/workfl	1 day	Thu 9/24/26	Thu 9/24/26		Jonathan Wesley
37		2.3.3 Assign tasks to team	1 day	Fri 9/25/26	Fri 9/25/26		Jennifer Sanchez
38		2.3.4 Establish coding and documentation standards	1 day	Mon 9/28/26	Mon 9/28/26		Conner Cowles,Jennifer Sanchez,Jonathan Wesley,Paul




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
39		**Phase 3: Core Feature Development**	**17 days**	**Mon 10/5/26**	**Tue 10/27/26**		**Conner Cowles,Jennifer Sanchez,Jonathar**
40		**3.1 User Authentication & Roles**	**5 days**	**Mon 10/5/26**	**Fri 10/9/26**		**Jonathan Wesley**
46		**3.2 Employee Management**	**7 days**	**Mon 10/12/26**	**Tue 10/20/26**		
52		**3.3 Onboarding Workflow**	**6 days**	**Mon 10/12/26**	**Mon 10/19/26**		
58		**3.4 Offboarding Workflow**	**5 days**	**Mon 10/12/26**	**Fri 10/16/26**		
64		**3.5 Equipment Inventory**	**6 days**	**Fri 10/16/26**	**Fri 10/23/26**		
70		**3.6 Dashboard**	**4 days**	**Mon 10/19/2**	**Thu 10/22/2**		
76		**3.7 Help Desk**	**5 days**	**Mon 10/19/2**	**Fri 10/23/26**		
82		**Phase 4: Integration & Testing**	**5 days**	**Mon 10/26/26**	**Fri 10/30/26**		
84		**Phase 5: Delivery and Final Presentation**	**1 day**	**Tue 9/15/26**	**Tue 9/15/26**		



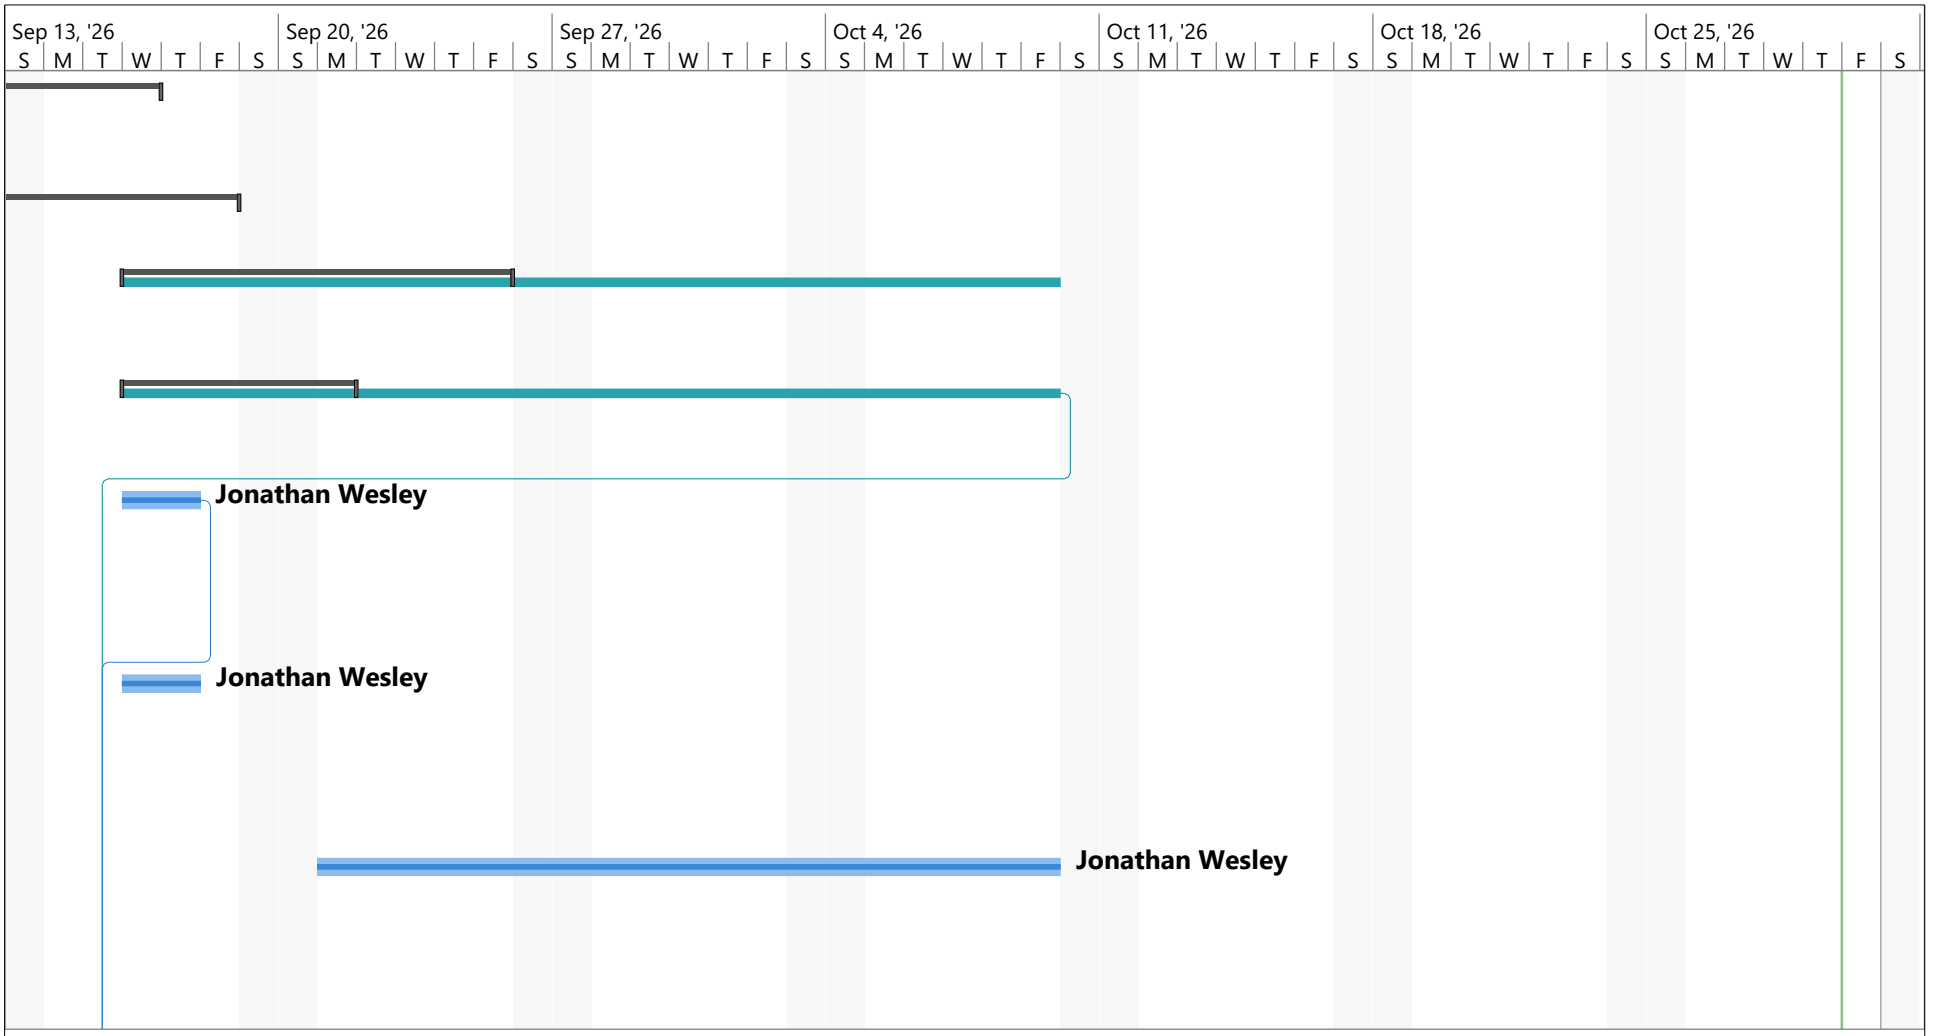


Project: IT Capstone Project- Iss
Date: Fri 10/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

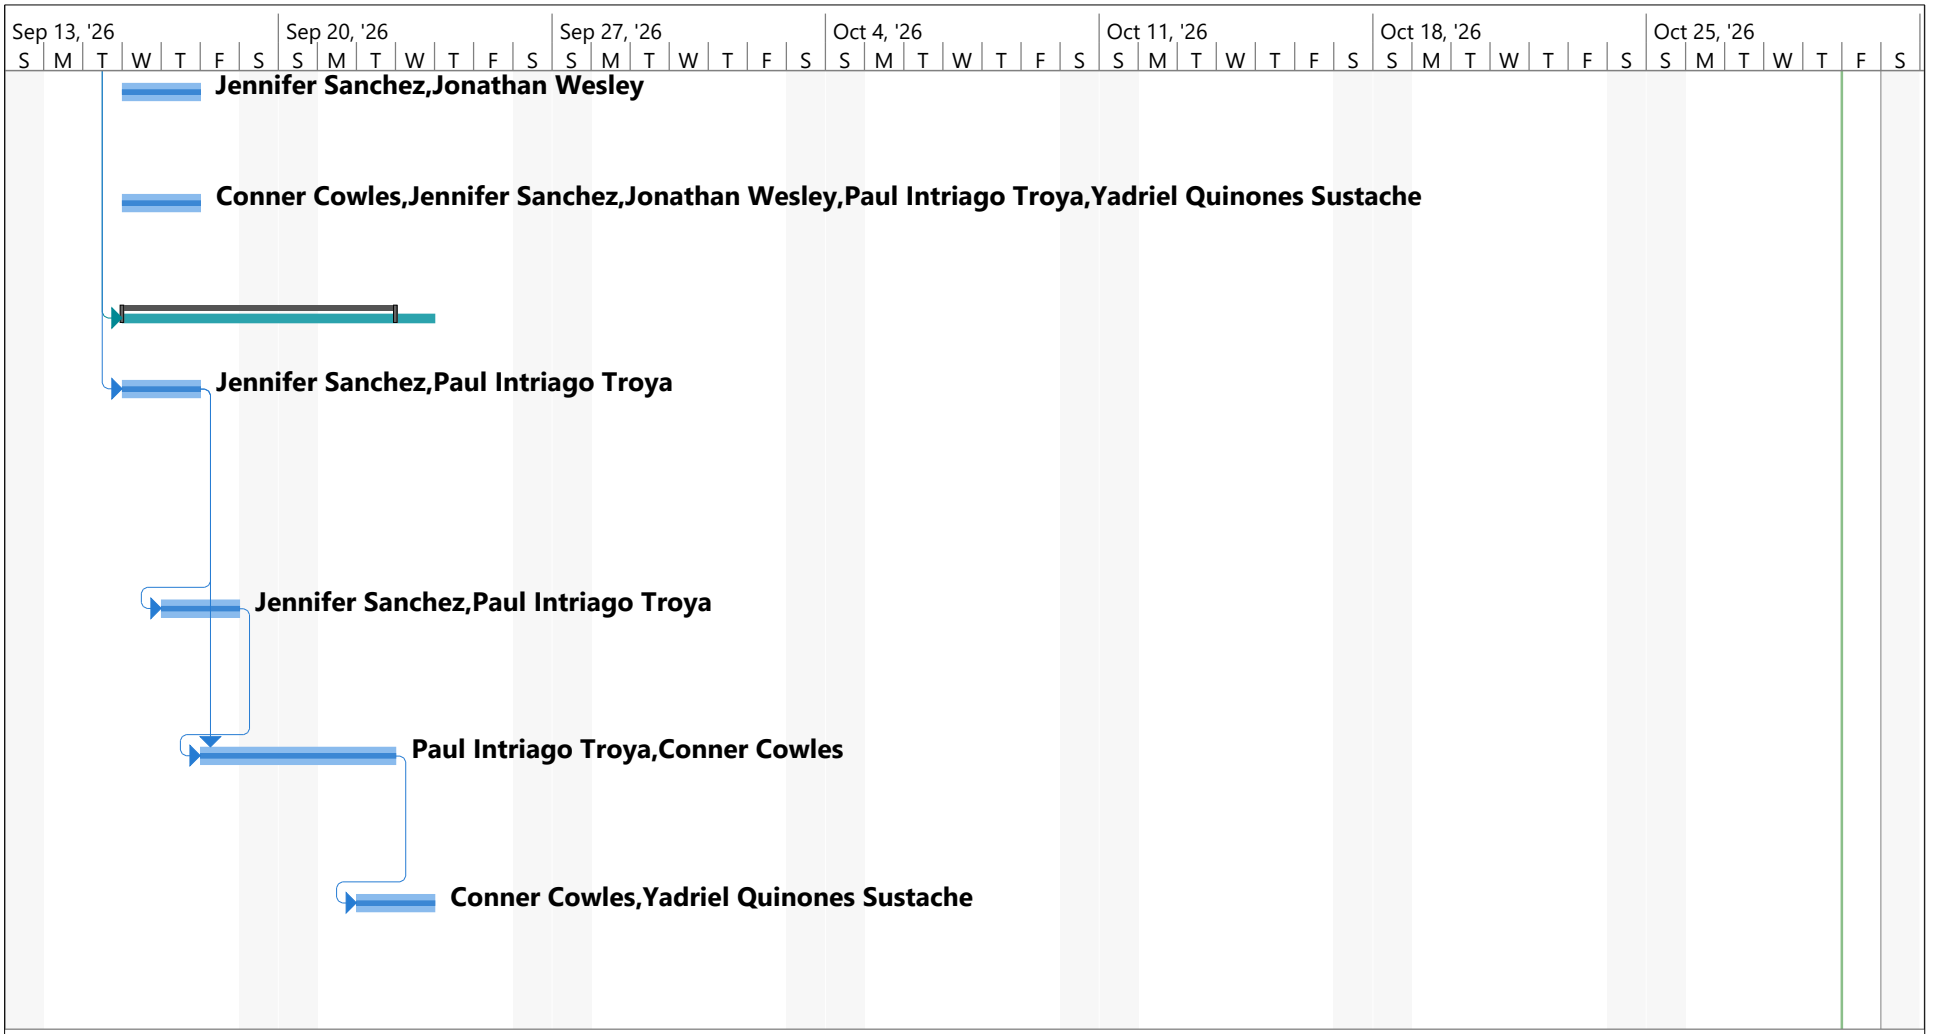


Project: IT Capstone Project- Iss
Date: Fri 10/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

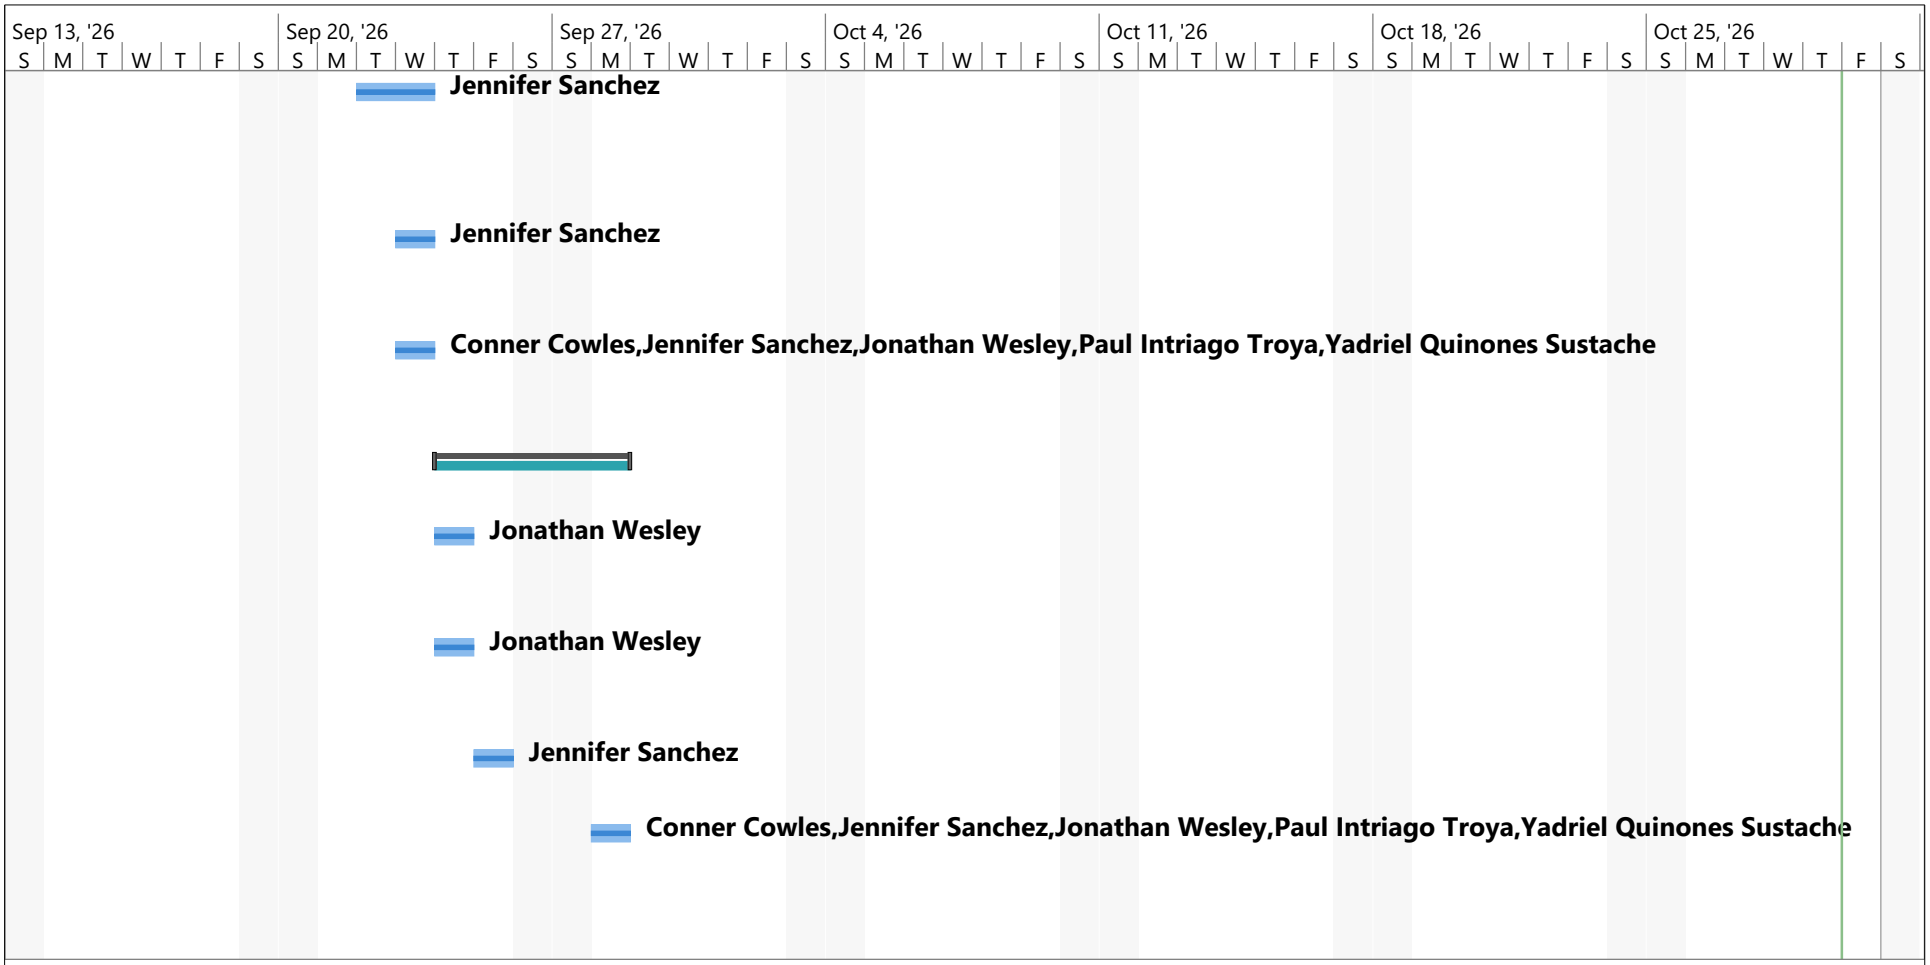

Project: IT Capstone Project- Iss
Date: Fri 10/30/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

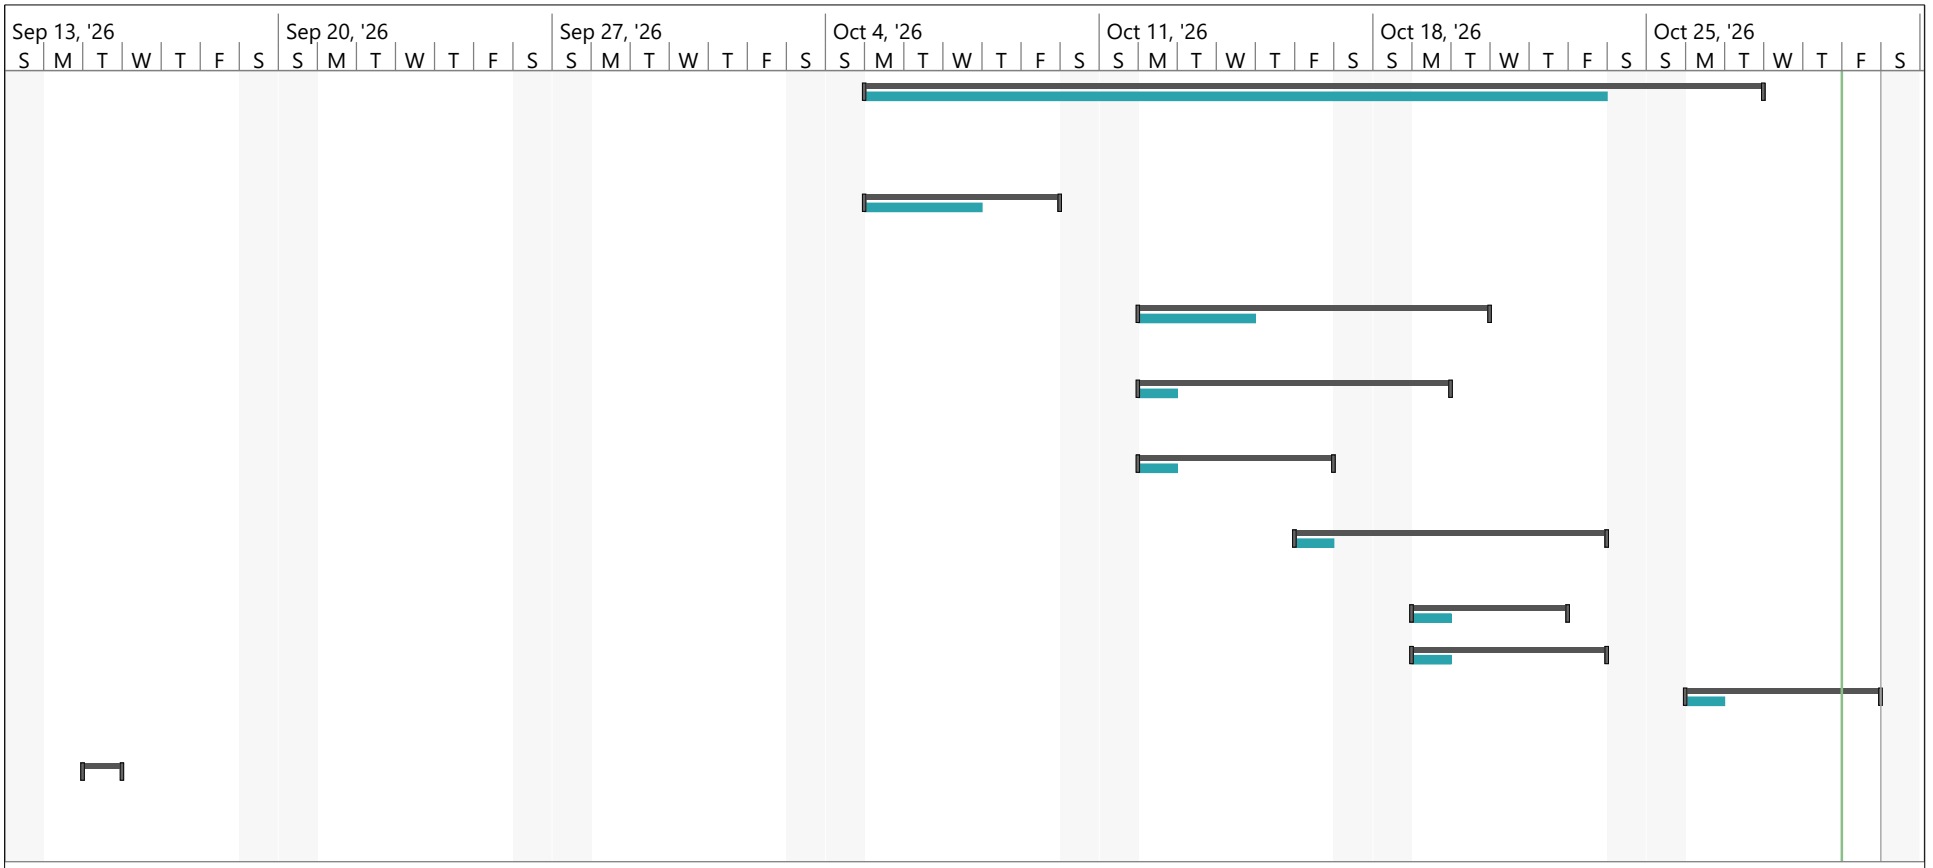

Project: IT Capstone Project- Iss
Date: Fri 10/30/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	
